



SELF INSPECTION SHEET

CONFIDENTIAL INFORMATION

This document and the information contemplated therein have to be considered as Confidential Information pursuant to the provisions of Clause 25 of the MSA, and treated as such.

APPLICATION REFERENCE

MOUNTING	DESCRIPTION	STATION	CAR TYPE						WORK INSTRUCTION	SAFETY?	
			TC1	M4	M1	M2	M3	TC2			
<input type="checkbox"/>	DTR3-PROCE-14	LEVELLING, WEIGHTING AND BALANCING M CAR	FT1140		1	1	1	1		PRA.FT1140.04	YES
<input type="checkbox"/>	DTR3-PROCE-14	LEVELLING, WEIGHTING AND BALANCING TC CAR	FT1140	1					X	PRA.FT1140.05	YES
<input type="checkbox"/>	DTR3-PROCE-17	LEVELLING, WEIGHTING AND BALANCING TC CAR	FT1140	1	1	1	1	1	1	PRA.FT1140.05	YES
<input type="checkbox"/>	DTR3-PROCE-17	LEVELLING, WEIGHTING AND BALANCING TC CAR	FT1140	1	1	1	1	1	1	PRA.FT1140.05	YES
<input type="checkbox"/>											
<input type="checkbox"/>											
<input type="checkbox"/>											

REV	DATE	MODIFICATION CONTENT	RESPONSIBLE	NAME	DATE
7	2/11/2020	UPDATE OF AIR TIGHTNESS TEST TIME FROM 4 MIN TO 5 MIN. ADD PANTOGRAPH AIR TIGHTNESS.	APPROVER	GIVEN SILOWA	2/11/2020
			CHECKER	SIMON MOKOENA	2/11/2020
			COMPILER	COMFORT MALATJI	2/11/2020
8	9/13/2021	ADDING GAUGE MEASUREMENT CHECK ON THE SI.	APPROVER	MAKOFANE LUCY	9/13/2021
			CHECKER	RATAU EDISON	9/13/2021
			COMPILER	TSAKANI KHOSA	9/13/2021
9	5/31/2022	pressure valve (APV) Isolation	APPROVER	MAKHURUPETJI THABANG	5/31/2022
			CHECKER	HAZEL MGIBA	5/31/2022
			COMPILER	RATAU EDISON	5/31/2021

TUE	CAR	OPERATOR NAME	DATE	SELF INSPECTION NUMBER	PAGES
T/S 230	TC2	Mamba	19/06/24	SI.FT1140.52	01/08



SELF INSPECTION INDUSTRIAL QUALITY

Rev:09

Date:

5/31/2022

Projet:
PRASA

SI.FT1140.52

Car:

MCR:

Work Station

FT1140



Safety Related


1 - Document and Instrument Control

1.1 - Documents control

Document	TC	RI	VC	RS	RA	TC	Revision	Remark	OK	Signature/Date
PRA.FT1140.04						✓			✓	
PRA.FT1140.05										19/06/22
PRA.FT1140.06										

1.2 - Instruments Control - Monitoring and Measuring Instrument Control (Used for all Instrument with calibration needed)

Instruments description	Serial number	Calibration or Verification Validation Date	OK	Signature/Date	
MEASURING TAPE	GISTA 0276	26/06/23-26/10/24	✓		
Vernier Caliper	GIBUR 0056	06/06/23-06/06/24	✓		
torque wrench 35NM	D2811623	19/12/21-19/12/24	✓		
torque wrench 150NM	D28122009	19/12/21-19/12/24	✓		
torque wrench 320NM	A9650027	21/12/23-21/12/24	✓		
torque wrench 520NM	A9630053	21/12/23-21/12/24	✓		19/06/22
torque wrench 17NM	D2801617	19/12/21-19/12/24	✓		





SELF INSPECTION INDUSTRIAL QUALITY

Rev:09

Date:

5/31/2022

Project: PRASA

SI.FT1140.52

II - Self Inspection - Items to Check

II.1 - Items to Check

Item	Picture/Sketch	Description	Criteria/Record	OK	Not OK	Signature/Date
01		Ensure that the average pressure valve (APV) is isolated by capping the two input pipes at the fittings installing the blanking fitting on the pipes highlighted.		<input checked="" type="checkbox"/>		<i>[Signature]</i> 19/06/24
02		Check underframe pipe system Air tightness. Test performance according to WI PRA_FT1130.15.	The test was performed and no leak was observed. Initial pressure (IP): 16.25 bar Final pressure (FP): 16.02 bar FP - IP = 0.03 bar APPROVAL CRITERIA: After 5 minutes the pressure cannot drops more than 0,2 bar	<input checked="" type="checkbox"/>		<i>[Signature]</i> 19/06/24
03		Movement performed at least 50m to shudder the car. And position on the leveled load cell, with wheels on the center.		<input checked="" type="checkbox"/>		<i>[Signature]</i> 19/06/24
04		Measurement inspection was done with car on condition AWO and the rail levelled. (The load cells system must be levelled and calibrated)	Calibration Validation Date 19/11/23	<input checked="" type="checkbox"/>		<i>[Signature]</i> 19/06/24
05		In case of the equipments not installed, equivalent weight of the item should be added in the same place to simulate the equipment. (Any simulated weight, add on pending list)	EQUIPMENT DESCRIPTION DRIVER SEAT WEIGHT (kg) 60	<input checked="" type="checkbox"/>		<i>[Signature]</i> 19/06/24
06		The pressure difference between air spring on each bogie when raise the pressure was maintained < 0.3 bar.		<input checked="" type="checkbox"/>		<i>[Signature]</i> 19/06/24
07		Measurement recorded with empty suspension and loaded are on conformity with tolerances of the project.		<input checked="" type="checkbox"/>		<i>[Signature]</i> 19/06/24
08		All levelling measurements are according to the reference. (Values out of reference must be recorded on "Description of defects")		<input checked="" type="checkbox"/>		<i>[Signature]</i> 19/06/24

GIBELG

03-19

CONTROLLED COPY



SELF INSPECTION INDUSTRIAL QUALITY

Rev:09

Date:

5/31/2022

Projet:
PRASA

SI.FT1140.52

Item	Picture/Sketch	Description	Criteria/Record	Signature/Date
09		Check that the leveling rods are torqued and have torque marker.		 19/06/24
10		The difference of weight between the left and right wheels of each axis, must be $\leq 4\%$. (Verify on the T&C equipment if all arrows are in green).		 19/06/24
11		Remove the car, move back onto the load cells and repeat the step 09. Confirm if both are in the tolerance of $\leq 4\%$.		 19/06/24
12		1 - Record shims thickness used on rod. 2 - All screws were torqued and have torque marker.	THICKNESS (mm) I II III IV	 19/06/24
13		Pivot fixation	1- M20 x 90 screws with application of torque according to PRA.FT1140.04 / 05	 19/06/24
14		FOR TC CARS F= Height of the center of Automatic coupler F = 895mm (+5 / -10mm) (Using levelled rail)	TC CAB #1= <u>896</u> mm	 19/06/24
15		FOR TC CARS Height of Eurobalise Antenna = 205mm(+/-10mm) (Using levelled rail)	TC CAB #1= <u>197</u> mm	 19/06/24
16		Check pantograph piping air tightness. Test performance according to WI PRA.FT1140.17.	The test was performed and no leak was observed. -Roof piping connection fittings. -Room piping connection fittings(Roof arch and door trimming)	TT/A
17		Pantograph does not come in contact with the higher height gauge when passing through.	No Contact with Pantograph and Gauge -GO Contact with Pantograph and Gauge - NO GO	TT/A
18		Car does not come into contact with the gauge.	No Contact with Car and Gauge -GO Contact with Car and Gauge - NO GO	 19/06/24

2024-05-19
CONTROLLED COPY



SELF INSPECTION INDUSTRIAL QUALITY

Rev:09
Date:
5/31/2022

Proj:
PRASA


SI.FT1140.52

DRAFT TO MEASUREMENTS DURING LEVELLING (ALL UNITS MUST BE IN mm/bar/kg)

DESCRIPTION	TOLERANCE	END#1												
		LEFT SIDE						RIGHT SIDE						
		6	5	4	3	2	1	1	2	3	4	5	6	
AIR SPRING HEIGHT (EMPTY)	N/A	A`ii												A`i
AIR SPRING HEIGHT (FULL)	min 254 max 261	Aii				257	258	257	258					Ai
FLOOR COVERING HEIGHT	min 1096 max 1116	Eii												Ei
AIR SPRING PRESSURE	≤ 0.3 {Ci - Ci}	Cii				361	369	361	289					Ci
PRIMARY SUSPENSION	SEE TABLE (ONLY REF)	D3												D1
PRIMARY SUSPENSION	SEE TABLE (ONLY REF)	D4												D2
PIVOT VERTICAL GAP	min 25 max 32	Ki												Ki
PIVOT LATERAL STOP GAPS DIFFERENCE	≤ 4 {Ji - Ji}	Jii												Ji
QTY OF TURNS OF LEVELLING ROD	N/A	Xii				2 1/4		0						Xi
SHIMS OF ANTI-ROLL BAR	N/A	Yii												Yi
DESCRIPTION	TOLERANCE	END#2												
		LEFT SIDE						RIGHT SIDE						
		6	5	4	3	2	1	1	2	3	4	5	6	
AIR SPRING HEIGHT (EMPTY)	N/A	A`iii												A`iv
AIR SPRING HEIGHT (FULL)	min 254 max 261	Aiii				258	259	261	257					Aiv
FLOOR COVERING HEIGHT	min 1096 max 1116	Eiii												Eiv
AIR SPRING PRESSURE	≤ 0.3 {Cv - Cv}	Ciii				289	283	290	361					Civ
PRIMARY SUSPENSION	SEE TABLE (ONLY REF)	D5												D7
PRIMARY SUSPENSION	SEE TABLE (ONLY REF)	D6												D8
PIVOT VERTICAL GAP	min 25 max 32	Kiii												Kiv
PIVOT LATERAL STOP GAPS DIFFERENCE	≤ 4 {Jiv - Jiv}	Jiii												Jiv
QTY OF TURNS OF LEVELLING ROD	N/A	Xiii				2 1/4		2 1/4						Xiv
SHIMS OF ANTI-ROLL BAR	N/A	Yiii												Yiv

COMPARE EACH TENTATIVE WITH THE TOLERANCE AND IDENTIFY EACH MEASURE AS BELOW

GOOD	LOWER	HIGHER
✓	↓	↑
WEIGHT COMPENSATION		
EQUIPMENT		
WEIGHT		
EQUIPMENT		
WEIGHT		
SECONDARY MEASUREMENTS (ONLY TC CARS)		
AUTOMATIC COUPLER HEIGHT		
ANTENNA HEIGHT		

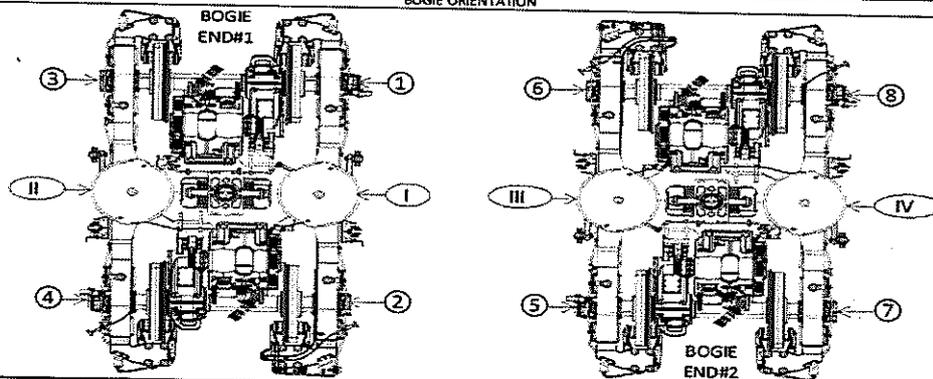

GIBELQ
2022-11
CONTROLLED COPY



SELF INSPECTION INDUSTRIAL QUALITY

Rev:09

Date:

5/31/2022

Proj:
PRASA




SI.FT1140.52

DRAFT TO MEASUREMENTS DURING LEVELLING (ALL UNITS MUST BE IN mm/bar/kg)

DESCRIPTION	TOLERANCE	END#1												
		LEFT SIDE						RIGHT SIDE						
		6	5	4	3	2	1	1	2	3	4	5	6	
AIR SPRING HEIGHT (EMPTY)	N/A	A ⁱⁱ												A ⁱ
AIR SPRING HEIGHT (FULL)	min 254 max 261	A ⁱⁱ												A ⁱ
FLOOR COVERING HEIGHT	min 1096 max 1116	E ⁱⁱ												E ⁱ
AIR SPRING PRESSURE	≤ 0.3 (C ⁱ - C ⁱ)	C ⁱⁱ												C ⁱ
PRIMARY SUSPENSION	SEE TABLE (ONLY REF)	D ³												D ¹
PRIMARY SUSPENSION	SEE TABLE (ONLY REF)	D ⁴												D ²
PIVOT VERTICAL GAP	min 25 max 32	K ⁱⁱ												K ⁱ
PIVOT LATERAL STOP GAPS DIFFERENCE	≤ 4 (J ⁱ - J ⁱ)	J ⁱⁱ												J ⁱ
QTY OF TURNS OF LEVELLING ROD	N/A	X ⁱⁱ												X ⁱ
SHIMS OF ANTI-ROLL BAR	N/A	Y ⁱⁱ												Y ⁱ
DESCRIPTION	TOLERANCE	6	5	4	3	2	1	1	2	3	4	5	6	
AIR SPRING HEIGHT (EMPTY)	N/A	A ⁱⁱⁱ												A ^{iv}
AIR SPRING HEIGHT (FULL)	min 254 max 261	A ⁱⁱⁱ												A ^{iv}
FLOOR COVERING HEIGHT	min 1096 max 1116	E ⁱⁱⁱ												E ^{iv}
AIR SPRING PRESSURE	≤ 0.3 (C ^{iv} - C ^{iv})	C ⁱⁱⁱ												C ^{iv}
PRIMARY SUSPENSION	SEE TABLE (ONLY REF)	D ⁵												D ⁷
PRIMARY SUSPENSION	SEE TABLE (ONLY REF)	D ⁶												D ⁸
PIVOT VERTICAL GAP	min 25 max 32	K ⁱⁱⁱ												K ^{iv}
PIVOT LATERAL STOP GAPS DIFFERENCE	≤ 4 (J ^{iv} - J ^{iv})	J ⁱⁱⁱ												J ^{iv}
QTY OF TURNS OF LEVELLING ROD	N/A	X ⁱⁱⁱ												X ^{iv}
SHIMS OF ANTI-ROLL BAR	N/A	Y ⁱⁱⁱ												Y ^{iv}

COMPARE EACH TENTATIVE WITH THE TOLERANCE AND IDENTIFY EACH MEASURE AS BELOW:

GOOD	LOWER	HIGHER
✓	↓	↑
WEIGHT COMPENSATION		
EQUIPMENT		
WEIGHT		
EQUIPMENT		
WEIGHT		
SECONDARY MEASUREMENTS (ONLY TO CARS)		
AUTOMATIC COUPLER HEIGHT		
ANTENNA HEIGHT		

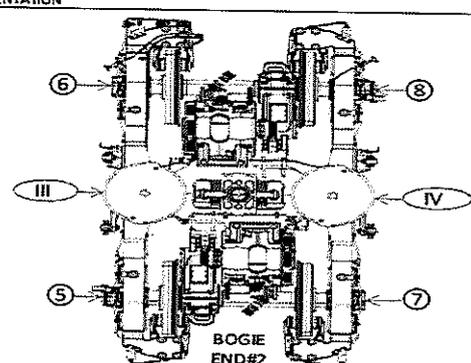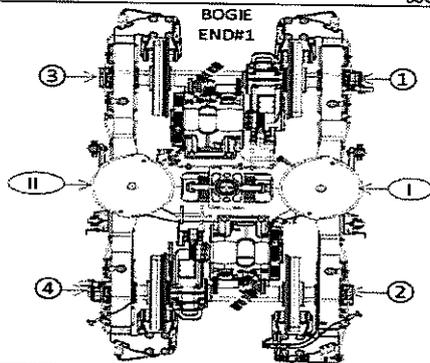



SELF INSPECTION INDUSTRIAL QUALITY


Rev:09
Date:
5/31/2022

Projct:
PRASA

SI.FT1140.52

Table 1 - Reference Values and Measurement Tolerances for the Car Levelling.

ITEM	THEORETICAL VALUES													
	TCL CAR		M4 CAR		M3 CAR		M2 CAR		M3 CAR		T12 CAR			
	TBext	TBint	MB1	MB2	MB1	MB2	MB1	MB2	MB1	MB2	TBint	TBext		
Phot lateral stop gaps difference (mm)	≤4	≤4	≤4	≤4	≤4	≤4	≤4	≤4	≤4	≤4	≤4	≤4	≤4	
Air Spring height (mm)	255 ⁺⁶ ₋₄													
Air spring pressure at AWP (bar)	3,76 (Ref.)	2,82 (Ref.)	2,87 (Ref.)	2,83 (Ref.)	3,02 (Ref.)	2,91 (Ref.)	3,07 (Ref.)	2,85 (Ref.)	2,83 (Ref.)	2,87 (Ref.)	2,83 (Ref.)	2,83 (Ref.)	3,76 (Ref.)	
Primary Suspension gaps (mm)	0,3 Mlx.													
	35 ⁺¹¹ ₋₄													
	D ₁₂ D ₈													
	D ₁₄ D ₇													
Carbody Floor height (mm)	1106 ⁺¹⁰ ₋₁₀													
Boiler height (mm)	850 ⁺⁵ ₋₇													
Coupling End height (mm)	895 (Ref.)	760 (Ref.)	895 (Ref.)	760 (Ref.)	760 (Ref.)									
	760 (Ref.)													
Pivot Vertical gap (mm)	30 ⁺¹⁵ ₋₅													
	30 ⁺¹⁵ ₋₅													





SELF INSPECTION INDUSTRIAL QUALITY

Rev:09

Date:

5/31/2022

Projct:
PRASA

SI.FT1140.52

Leveling report from Production (Final measurements after Leveling and Weighting fine)

References for secondary suspension empty
A'n Air spring height empty



References for secondary suspension full
An Air spring height
Bn Difference between measurement A'n and An
En Floor covering height
Cn Air spring pressure
Dn Primary suspension
Kn Pivot Vertical gap
Jn Pivot Lateral stop gaps difference

Item	Reference [mm]	END#1		END#2	
		Right Side	Left Side	Left Side	Right Side
A'n	N/A	A'i 255	A'ii 233	A'iii 241	A'iv 242
An	254 to 261	Ai 257	Aii 256	Aiii 258	Aiv 257
Bn = An - A'n	N/A	Bi 22	Bii 23	Biii 17	Biv 15
En	1106 ±10 mm	Ei 1109	Eii 1107	Eiii 1109	Eiv 1107
Item	Reference [bar]	END#1		END#2	
Cn	Table 02 (*)	Ci 3,64	Cii 3,58	Ciii 2,83	Civ 2,79
Cn - Cn+1	Diference ≤ 0,3	Ci - Cii 0,06		Ciii - Civ 0,04	
Gauge serial number	N/A	G1B05873	G1B05873	G1B05874	G1B05874
Item	Reference [mm]	END#1		END#2	
Dn	Table 01 (*)	D1 42,15	D2 42,97	D3 43,66	D4 44,15
		D5 43,27	D6 43,19	D7 44,77	D8 45,26
Kn	25 to 45	Ki 31,99	Kii 26,59	Kiii 34,76	Kiv 24,62
Jn	Diference ≤ 4	Ji 26,06	Jii 26,59	Jiii 25,75	Jiv 24,62

(*) Reference, only include values, isn't approval criteria.

Table 01 D Theoretical Values	TC1		M4		M1		M2		M3		TC2	
	Tbox	TBin	Mb1	Mb1	Mb1	Mb2	Mb2	Mb1	Mb1	Mb1	Tbin	Tbox
D=	$35 \frac{+12}{-5}$											

Table 02 C Theoretical Values	TC1		M4		M1		M2		M3		TC2	
	Tbox	TBin	Mb1	Mb1	Mb1	Mb2	Mb2	Mb1	Mb1	Mb1	Tbin	Tbox
C=	3.76	2.82	2.87	2.83	3.02	2.91	3.07	2.85	2.83	2.87	2.83	3.76

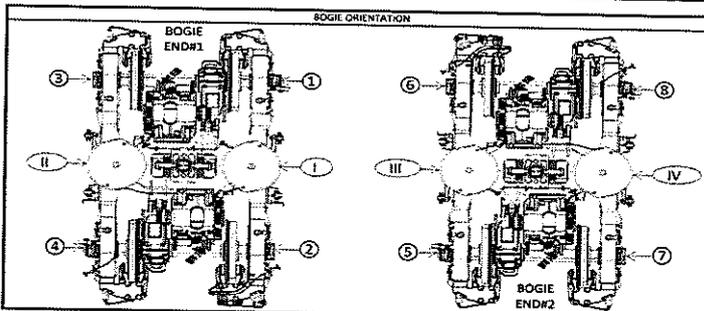

Weighting report from Test and Commissioning (Final measurements after Leveling and Weighting fine)

